



Training Area 5: Clearing and Grading Project Update

USACE BRAC Area Office

14 September 2007

Project Description

Provide site clearing and grading at Training Area 5, Fort Lee, Virginia. Site work includes timbering, clearing, grading, installation of erosion and sediment control ponds, devices and related work, demolition of metal earth covered magazines, and related walls and foundation, removal of fencing and miscellaneous concrete pads and pavement, installation of new security fencing and temporary fencing, roadwork, and related site and utility work.

Contractor: Fort Sill Apache Industries

Contract Value: \$10,641,000

Contract Duration: 150 days

Notice to Proceed: 01 Aug 2007

Contract Completion Date: 29 Dec 07

Project Delivery Team

U.S. ARMY CORPS OF ENGINEERS

- Bill Robson
- Anthony Weaver
- Ed Graham
- Candice Filak
- Bruce Anderson
- Jerry Williams
- Manny Ante
- Norm Malbon
- Laurie Neitzke
- Jen Armstrong

FORT SILL APACHE/ PHILLIPS & JORDAN


- Richard Lewis
- Pat Williams
- Rodney Poe
- Tom Tinics
- Randall Stanley

U.S. ARMY, FORT LEE, VIRGINIA

- Colonel Ed Gully
- Dana Bradshaw
- Al Cruz
- Carol Anderson
- John Royster

Project Schedule

Scheduled Placement- Construction S Curve

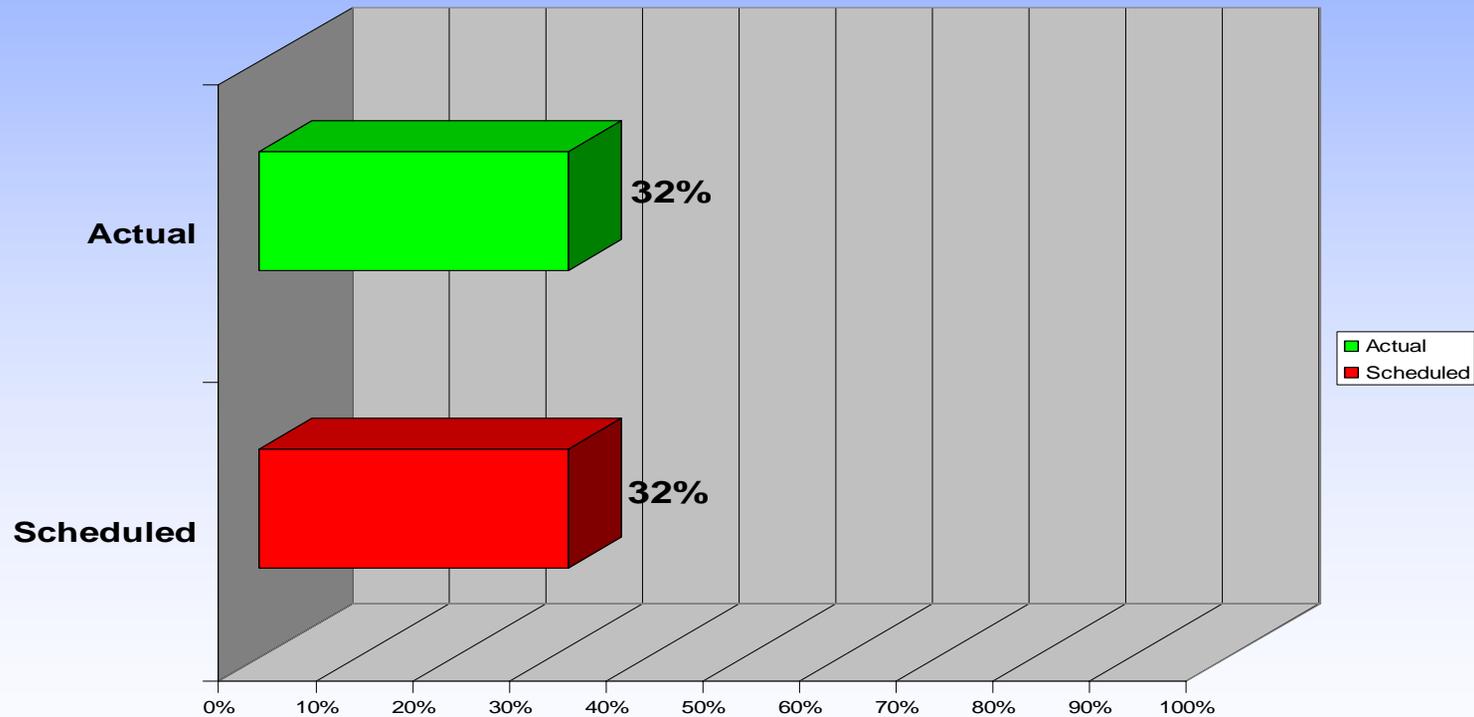



**Tree cutting
machine**

11 August 2007



**Partial timber
harvest:
approximately 16
trailers per day**

2007 8 11

11 August 2007

**Erosion control
measures adjacent to
sensitive
environmental areas.**





09.03.2007



**Erosion control pond
intake structure**

09.05.2007



**Nuclear testing of
detention basin soil**

09.05.2007



**Uncovered
ammunition bunker**

09.12.2007

04 September 07



Temple Road

River Road

Route 36



04 September 07

Jackson Circle



River Road closed on 20 August 2007

Temple Road

